

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	13-Sep-08	75

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu,	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutio.	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (F)		Wind		Add'l Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low	71			Precip. (in/Dy)	
				High	97	NW	3mph	Humidity (%)	
Additional Weather Comments Calm to light wind.									

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager. CM	Construction Management Services.	N
Dave Gertz	Project Engineer	Construction Management Services.	N
June Laubinger	Admin Assistant	Construction Management Services.	N
Linda Nations	Asst Const Manager	Construction Management Services	Y

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Wayne Wofford	QA/QC Tech	Oversight	N
Brent Barbacane	QA/QC Tech	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Greg Corcoran	Engineer of Record	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Camon Liddell	QA/QC Tech	Oversight	N
Dan Street	QA Manager	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	Y
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Scott McKeag, McGinley	Oversight	For NDEP	N
Devin Gordon, McGinley	Oversight	For NDEP	N
Dock Kim, ATC	Field Observation	For AIG	Y
Ron Perry, ASW	Inspector	Liner Inspector	N
PBS&J, Survey	Surveyors	Surveying	N
Brian Rakvica	Inspector	NDEP	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	Y
Josh Carrol	Entact	Asst Project Manager	Y
Russ Karnes	Entact	Eastside, Superintendent	Y
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	N
	Entact	22 Equipment Operators & Truck Drivers	Y
Ed Long	Entact	CAMU, Superintendent	Y
	American Asphalt	1Earthwork Superintendent, Power Screener	Y
	American Asphalt	1 Equipment Operator, Power screener	Y
Rick McIntire	Entact	CSP, Safety	N
	Environmental Specialties, Inc	Liner Superintendent	N
	Environmental Specialties, Inc	Laborers/ Seamers	N
	Kenney Survey	CAMU	N

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	13-Sep-08	75

ABC Survey	Eastside/CAMU	N	

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (2)		CAMU	-	-	-	-
JD D400 Dump Trucks (6)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (2)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (6)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Wagon		CAMU				-
CAT D-6 Dozer		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
Bobcat Skidsteer		CAMU				-
JLG		CAMU				-
CAT D4 dozer		CAMU				-
						-
						-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	QTY	UOM	Purpose	Delivery Verification			
					Condn	Qty	Spec	Tans
GCL	CETCO	0	rolls	For CAMU				
Geocomposite	Agru	0	rolls	For CAMU				
Geomembrane	Agru	0	rolls	For CAMU				

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

- Loaded out wet soils from SW-5 with CAT 345 excavator (4) trucks hauled 149 loads @ 20 cy/load = 2,980 cy. Spreading at dry ponds.
- Tractor and pans - 48 loads @ 30 cy/loads = 1,440 cy prepared material - 1 tractor.
- Watered haul Rds and Maintained them with 4,000 gal Water truck and Motorgrader.
- CAT 324 Long Stick excavator, No activity. Being repaired.
- Continued pumping water from SC-1 to SW-12.
- D6 Dozer and 2nd Water truck continued roughing in haul roads on dry ponds, east side.
- Electricians worked on installing conduit between the H-structure and the trailers for phone lines.

CAMU Activity:

Excavation

- Excavated excess western ditch material from area south of Phase 1. Scraped access road ramp leading into Phase 1.
- Phase 2, excavated silt and sediment from potholes, backfilled with rock to 1 foot above water level. Left open to check recharge.
- Screened 1" minus clean soil from 200,000 yd stockpile and used it to place on the Northeast bench between phase 1 and phase IIIB. To cover the geomembrane.
- Continued fence installation in Tronox and Timet property for haul road construction.

Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy

Waste Placement

- Phase 1 estimated daily waste placed: 0 cy
- Phase 1 estimated cumulative waste placed: 0 cy
- Phase 1 Operations Layer placed, completed.

Geosynthetics.

- Phase 1 GCL placed: 0 sf daily, 347,067 sf cumulative.
- Phase 1 Geomembrane: 0 sf daily, 365,136 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 327,600 sf cumulative.
- Phase 1 Geotextile: (0) sf daily..

Other:

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	13-Sep-08	75

--

HEALTH & SAFETY

Description of Health & Safety Actions Taken Today / Safety Inspections Conducted

Entact H&S Tailgates

Morning: Snakes and coyotes..

Safety Incidents: No Incidents.

QUALITY CONTROL	
1	100%
2	100%
3	100%
4	100%
5	100%
6	100%
7	100%
8	100%
9	100%
10	100%
11	100%
12	100%
13	100%
14	100%
15	100%
16	100%
17	100%
18	100%
19	100%
20	100%
21	100%
22	100%
23	100%
24	100%
25	100%
26	100%
27	100%
28	100%
29	100%
30	100%
31	100%
32	100%
33	100%
34	100%
35	100%
36	100%
37	100%
38	100%
39	100%
40	100%
41	100%
42	100%
43	100%
44	100%
45	100%
46	100%
47	100%
48	100%
49	100%
50	100%
51	100%
52	100%
53	100%
54	100%
55	100%
56	100%
57	100%
58	100%
59	100%
60	100%
61	100%
62	100%
63	100%
64	100%
65	100%
66	100%
67	100%
68	100%
69	100%
70	100%
71	100%
72	100%
73	100%
74	100%
75	100%
76	100%
77	100%
78	100%
79	100%
80	100%
81	100%
82	100%
83	100%
84	100%
85	100%
86	100%
87	100%
88	100%
89	100%
90	100%
91	100%
92	100%
93	100%
94	100%
95	100%
96	100%
97	100%
98	100%
99	100%
100	100%

Description of Quality Control Actions Taken Today / Quality Inspections Conducted

Daily CQA Summary.

Inspected 12" capped haul roads for degradation. All areas ok.
Inspected Phase 2 potholes. Mucked out silt and backfilled with rock above water level.

Dust: Met requirements.

<u>Deviations from CQA Plan</u> None	
---	--

ISSUES AND/OR ITEMS OF DISCUSSION

Discussion of Issues / Concerns / Conversations / Topics

SITE VISITORS

[illegible]

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Dick Laubinger, Construction Manager 13-Sep-08

Date Prepared _____ Signature _____

13-Sep-08

Signature: _____

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	13-Sep-08	75


DAILY PHOTO LOG

Photo 1



CAMU, Phase 1 scraping ramp of potentially contaminated soils.

Photo 2

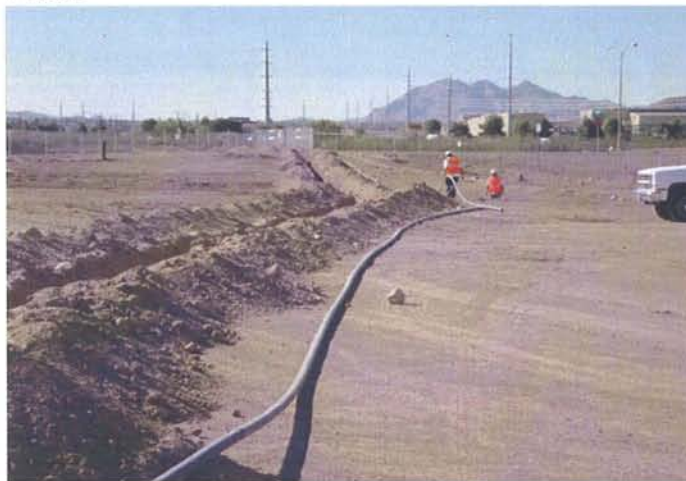

Eastside, Installing electrical conduit. To project trailers.

Photo 3



Eastside: Fence stolen Friday night 9-12-08. Southeast side.

Photo 4



CAMU: Phase 2, potholes. Silt and sediment removed backfilled with rock above water level.
