

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	27-Sep-08	87

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu,	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.c	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (°F)	Wind	Add'l Readings	
AM	Sunny / Party Cloudy	PM	Sunny / Party Cloudy	Low 74		Precip. (in/Dy)	
				High 98	E 9mph	Humidity (%)	
Additional Weather Comments Calm to light winds.							

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Dick Laubinger	Construction Manager	Construction Management Services.	Y	
Dan Brennecke	Project Manager, CM	Construction Management Services.	N	
Dave Goertz	Project Engineer	Construction Management Services.	N	
Richard Davis	Project Engineer	Construction Management Services.	N	
Chris White	Assist. Const. Mgr	Construction Management Services.	Y	
	Assist. Const. Mgr	Construction Management Services.		
June Laubinger	Admin Assistant	Construction Management Services.	N	

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Greg Corcoran	Engineer of Record	Oversight	N	
Dan Street	QA Manager	Oversight	Y	
Jim Cox	QA/QC Supervisor	Oversight	N	
Robecca Flynn	Engineer	Oversight	N	
Wayne Wofford	QA/QC Tech	Oversight	N	
Brent Barbacane	QA/QC Tech	Oversight	N	

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring,	N	
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring,	Y	
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Scott McKeag, McGinley	Oversight	For NDEP	N	
Devin Gordon, McGinley	Oversight	For NDEP	N	
Dock Kim, ATC	Field Observation	For AIG	Y	
Ron Perry, ASW	Inspector	Liner Inspector	N	
PBS&J, Survey	Surveyors	Surveying, QA	N	
Brian Rakvica	Inspector	NDEP	N	

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N	
Erik Geringer	Entact	Project Manager	Y	
Josh Carrol	Entact	Asst Project Manager	Y	
Russ Karnes	Entact	Eastside, Superintendent	Y	
Michael Carlson	Entact	Engineer	Y	
Joe Curilla	Entact	Health & Safety Officer	N	
Timothy Stadt	Entact	Health and Safety Technician	Y	
	Entact	24 Equipment Operators & Truck Drivers	Y	
Ed Long	Entact	CAMU, Superintendent	Y	
	American Asphalt	1 Superintendent	N	
	American Asphalt	3 Equipment operators	N	
Rick McIntire	Entact	CSP, Safety	N	
	Environmental Specialties, Inc	Liner Superintendent	N	

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	27-Sep-08	87

Environmental Specialties, Inc	Laborers/ Seamers	N	
Kenney Survey	CAMU	N	
ABC Survey	Eastside/CAMU	Y	

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (2)		CAMU	-	-	-	-
JD D400 Dump Trucks (6)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (2)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (6)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Wagon		CAMU				-
CAT D-6 Dozer		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		Eastside and CAMU				-
Tenent Street Sweeper		Eastside and CAMU				-
						-
						-
						-
						-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	QTY	UOM	Purpose	Delivery Verification			
					Condn	Qty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU				
Geocomposite	Agro	0	rolls	For CAMU				
Geomembrane	Agro	0	rolls	For CAMU				

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

- Loaded out wet soils from SW-10 with CAT 345 excavator (4) trucks hauled 125 loads @ 20 cy/load = 2,500 cy. Spreading at HP-5..
- D6 dozer spread wet material from SW-10 on dry ponds.
- D8 dozer and disk working wet material previously placed at dry ponds.
- Tractor and pans - 64 loads @ 30 cy/loads = 1,920 cy prepared material. (1) tractor.
- Watered haul Rds and Maintained them with 4,000 gal Water truck and 14H Motorgrader.
- Continued pumping water from SC-1 to SW-12.
- D6N dozer worked on haul roads East of the sewer alignment (supported by 4,000 gal water truck).
- Worked on the construction of the decontamination pad rinse water storage ponds.

CAMU Activity:

Excavation

- Phase 2 excavation , north of western ditch, (0) scrapers, hauled 0 cy.
- Continued fence installation in Tronox and Timet property for haul road construction.
- Installing main gate at West Warm springs Rd, along with fence tie-in.
- Hauled 82 loads = 1,230 cy with (2) dump truck from stockpile to haul roads. D6 dozer developing haul roads. Water truck supporting.
- Continued screening 6" minus material for future cover soil and engineered fill.
- Phase 2 screening 6" minus material for future placement. At phase 2 floor.

Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy

Waste Placement

- Phase 1 estimated daily waste placed: 0 cy
- Phase 1 estimated cumulative waste placed: 0 cy
- Phase 1 Operations Layer placed, completed.

Geosynthetics. Estimated cumulative installed quantity by Phase.

- Phase 1 GCL placed: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geomembrane:0 sf daily, 307,372 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 307,372 sf cumulative.

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	27-Sep-08	87

- Phase 1 Geotextile: (0) sf daily. 69,340 sf cumulative.

Other: Construction Office Trailers:
Electrician completed working on the installation of telephone and high speed internet.
Excavated trench for conduit installation for permanent power in parking area to construction trailers.

HEALTH & SAFETY

Description of Health & Safety Actions Taken Today / Safety Inspections Conducted

Entact H&S Tailgates

Safety Topic: Complacency, 6th day of work. Stay alert.

Safety Incidents: None.

CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

Description of Quality Control Actions Taken Today / Quality Inspections Conducted

Daily CQA Summary.

Monitored site haul road maintenance and construction of new 12" capped haul roads.
Provide oversight at the CAMU regarding screening of native soils at the site stockpiles for the production of engineered fill.
Routinely monitor storage procedures of the staged geosynthetics..
Continue review of Manufacturers Quality Control documentation and Quality Assurance conformance documentation.
Continue updating project documents and database to facilitate reporting.
Monitor fence installations.

ISSUES AND/OR ITEMS OF DISCUSSION

Discussion of Issues / Concerns / Conversations / Topics

SITE VISITORS

[illegible]

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Date Prepared	Signature
---------------	-----------

Signature _____

Dick Laubinger, Construction Manager 27-Sep-08

27-Sep-08

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	27-Sep-08	87


DAILY PHOTO LOG

Photo 1



Eastside: Trenching excavated for electrical power..

Photo 2

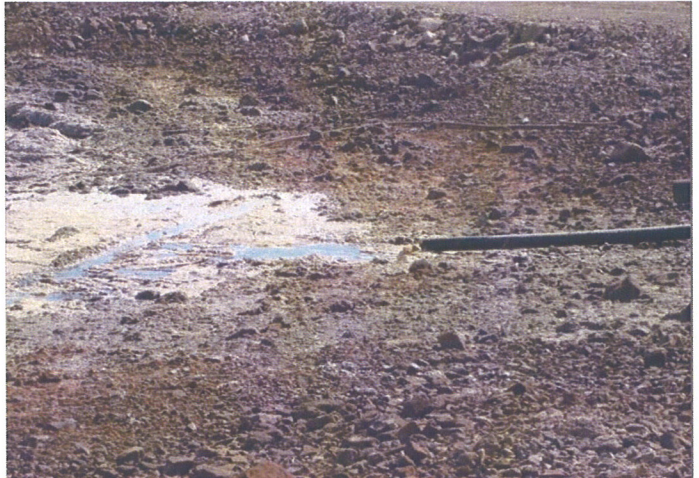

Eastside: Water discharge into SW-12 from SC-1.

Photo 3



Eastside: Loading out wet soils from SW-10.

Photo 4



Westside: Setting part of Main Gate. At exit haul road.
