## Basic Remediation Company 875 West Warm Springs Road Henderson, Nevada 89011



#### **DAILY PRODUCTION & QUALITY CONTROL REPORT** Report No. Day of Report Project No./Contract No. 6389 **BRC Eastside Common Areas Soils Remediation** 21-Jan-09 192

PROJECT POINTS OF CONTACT						
Position	Name	E-Mail Address	Phone No.			
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400			
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400			
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.d	970-260-5886			
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutio	720-641-8660			

	Condi	itions		Tem	(F)	W	ind	Add'l Readings
	T			Low	44			Precip. (In Dy.)
AM	Sunny / Party Cloudly	PM	Sunny / Party Cloudly	High	68	NNE	5mph	Humidity (%)

Calm to light winds. Light rain event overnight. No accumulation.

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager. CM	Construction Management Services.	Y
Richard Davis	Project Engineer	Construction Management Services.	Y
Chris White	Assist. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services.	Y
Kevin Cooke	Assist. Const. Mgr	Construction Management Services.	Y
June Laubinger	Admin Assistant	Construction Management Services.	Y

Position	Trade / Work Performed	Y/N
Design Engineer	Oversight	Y
QA Manager	Oversight	Y
QA/QC Supervisor	Oversight	N
Engineer	Oversight	N
QA/QC Tech	Oversight	N
QA/QC Tech	Oversight	Y
	QA Manager QA/QC Supervisor Engineer QA/QC Tech QA/QC Tech QA/QC Tech QA/QC Tech	QA Manager Oversight QA/QC Supervisor Oversight Engineer Oversight QA/QC Tech Oversight

r Monitoring Specialist	Air Monitoring	Y	
r Monitoring Specialist	Air Monitoring,	Y	
r Monitoring Specialist	Air Monitoring	Y	
r	Monitoring Specialist	Monitoring Specialist Air Monitoring,	Monitoring Specialist Air Monitoring, Y

OVERSITE PERSONNE			
Name	Position	Trade / Work Performed	Y/N
Mark Eizman, ASW	Inspector	Liner Inspector	Y
Devin Gordon, McGinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	Y
Joe Ludlow, ASW	Inspector	Liner Inspector	N
Steve Morrow, ASW	Inspector	Liner Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Surveying, QA, Phase IIIA subgrade.	Y
ON-SITE CONTRACTOR	PERSONNEL		
Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Josh Carrol	Entact	Asst Project Manager	Y
n 14			

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Josh Carrol	Entact	Asst Project Manager	Y
Russ Karnes	Entact	Eastside, Superintendent	Υ
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	Y
	Entact	26 Equipment Operators & Truck Drivers	Y
Ed Long	Entact	CAMU, Superintendent	Y
Lance Bruce	Entact	Health & Safety Officer	Y
Terry Harper	Entact	CAMU, Superintendent	Y
Rick McIntire	Entact	CSP, Safety	Υ
Dale Walsh	Converse	CSP, Safety	N
Eli Blackburn	Entact	Asst Project Manager	Υ
	Environmental Specialties,Inc	1 Liner Superintendent	Y
	Environmental Specialties,Inc	12 Laborers/ Seamers	Υ

1 of 4 Ver 1.1 11/07

### **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	21-Jan-09	192

Kenney Survey	CAMU	N
ABC Survey	Eastside/CAMU, Mohawk Drive.	Y

Equipment Vendor  CAT D400E Dump Truck (10)  JD D400 Dump Trucks (9)  CAT 324D long stick excavato  CAT D8R Dozer with disc  CAT 345 excavators, (5)  CAT 330 Excavator  Case double pan scrapers.  CAT D8 LGP Dozer (1)  Water Trucks (2)  JD450 Dozer	Tag No. Wo CAMU Eastside Eastside Eastside Eastside and CAM CAMU Eastside, demobili Eastside Eastside CAMU CAMU CAMU CAMU CAMU CAMU				
JD D400 Dump Trucks (9) CAT 324D long stick excavato CAT D8R Dozer with disc CAT 345 excavators, (5) CAT 330 Excavator Case double pan scrapers. CAT 06 LGP Dozer (1) Water Trucks (2)	Eastside Eastside Eastside Eastside and CAM CAMU Eastside, demobili Eastside CAMU				
CAT 324D long stick excavato CAT D8R Dozer with disc CAT 345 excavators, (5) CAT 330 Excavator Case double pan scrapers. CAT D6 LGP Dozer (1) Water Trucks (2)	Eastside Eastside Eastside and CAM CAMU Eastside, demobili Eastside Eastside CAMU				
CAT D8R Dozer with disc CAT 345 excavators, (5) CAT 330 Excavator Case double pan scrapers. CAT D6 LGP Dozer (1) Water Trucks (2)	Eastside Eastside and CAM CAMU Eastside, demobili Eastside Eastside CAMU			-	
CAT 345 excavators, (5) CAT 330 Excavator Case double pan scrapers. CAT D6 LGP Dozer (1) Water Trucks (2)	Eastside and CAM CAMU Eastside, demobili Eastside Eastside CAMU		-	-	
CAT 330 Excavator Case double pan scrapers. CAT D6 LGP Dozer (1) Water Trucks (2)	CAMU Eastside, demobili Eastside Eastside CAMU		-	-	
Case double pan scrapers.  CAT D6 LGP Dozer (1)  Water Trucks (2)	Eastside, demobili Eastside Eastside CAMU	ized.			
CAT D6 LGP Dozer (1) Water Trucks (2)	Eastside Eastside CAMU	ized.	-	-	
Water Trucks (2)	Eastside CAMU				
	CAMU				- 1
JD450 Dozer					
	CAMIL				
CAT 16H Grader	CAMU				
CAT D-10 Dozer	CAMU				
Water Trucks (2)	CAMU				
CAT D-6 Dozer, (2)	CAMU				
CAT 14H Grader	CAMU				
Gradall	CAMU				
JLG	CAMU				
IR Smooth drum Roller	CAMU, Phase 1				
Tenent Street Sweeper	Eastside and CAM	MU			
Bomag Smooth drum Roller	CAMU, Phase 1				
Chieftain 1400 Powerscreener	CAMU, screening	1"& 6" minus			

MATERIAL HANDLING	(ON-SITE DELIVERY / REMOVA	AL)					
Managari at	Vendor	Today	UOM	Purpose	Delivery Verification		cation
Material	Velidor	Today	OOW	ruipose	to date (	aty St	ec Tags
GCL	CETCO	0	rolls	For CAMU, On site	8	30	
Geocomposite	Agru	0	rolls	For CAMU, On site	9	39	
Geomembrane	Agru	0	rolls	For CAMU, On site	2	58	

### WORK COMPLETED

### Eastside Mixing and Drying Activity:

### Day Shift:

- Continue stockpiling/drying material in SW ponds.
- Continue pumping water from SW-7 to SW-12.
   Continue excavating in PUC-3 below the design excavation depth to 3 ft and hauling material to the Beta ditch stockpile area.
- Continue fabricating racks for air tanks to mount to the equipment for the slit trench work.
- Continued working on permanent lighting at decon pad. Eastside.
- Continued hauling material from HP-3 and PUC-3.

### CAMU Activity:

- Day Shift: ESI continued placing geocomposite on N. BMI Landfill.
- Continued excavating contaminated oil from NW Basin/Phase IIIB and placing in Phase II.

  Continued excavating contaminated soil from NW Basin/Phase IIIB and placing in Phase II.
- Continued placing 1" and 6" minus soils on N. BMI Landfill for cover material.
- Continued finish grading in Phase IIIA. (Northern Portion). Continued surficial scrape on Phase IIIB, IV and V and haul/place material to Phase II.
- Installed visqueen on Phase I North slope.
- Night Shift:
- Continued placing waste in Phase II.

- Phase 1 embankment, complete.
- Phase 1 estimated cummulative embankment placed: 0 cy
- Phase II embankment , complete.

### **Waste Placement**

- Phase 1 estimated daily waste placed: (0) loads @ 20 cy/load = 0 cy. (0 trucks).

- Priase 1 estimated daily waste placed: (0) loads @ 18cy/load = 0 cy.

   Phase 1 estimated cummulative waste placed: 291,020 cy.

   Phase 1 Operations Layer placed. completed. Cumulative total: 21,662

   Phase 2 estimated right shift placed: (261) loads @ 18cy/load = 4,518 cy, (19 trucks).

   Phase 2 estimated day shift placed: (76) loads @ 20 cy/load = 1,520 cy (Phase IIIB trench excavation). (4 trucks).
- Phase 2 Operations Layer placed. Cumulative total: 37,188 cy. Phase 2 estimated cummulative waste placed: 122,910 cy.

### Geosynthetics. Estimated cummulative installed quantity by Phase. - Phase 1 GCL placed:0 sf daily, 307,372 sf cummulative. - Phase 1 Geomembrane:0 sf daily, 307,372 sf cummulative.

- Phase 1 Geocomposite: 0 sf daily, 3,372 sf cummulative.
- Phase 1 Geotextile: (0) of daily. 69,340 of cummulative.

### **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	21-Jan-09	192
		21-Jan-09	192

- Phase 2 estimated cummulative waste placed: 122,910 cy.

Geosynthetics. Estimated cummulative installed quantity by Phase.

- Phase 1 GCL placed:0 sf daily, 307,372 sf cummulative
- Phase 1 Geomembrane:0 sf daily, 307,372 sf cummulative Phase 1 Geocomposite: 0 sf daily, 3,372 sf cummulative.
- Phase 1 Geotextile: (0) sf daily. 69,340 sf cummulative.
- -Phase 2 GCL placed: (0) sf daily, 498,468 sf cummulative. -Phase 2 Geomenbrane: (0) sf daily, 498,468 sf cummulative.
- Phase 2 Geocomposite: (0) sf daily, 520,592 sf cummulative.
  -BMI North Landfill GCL placed: (0) sf daily, 984,226 sf cummulative.
- BMI North Landfill Geomembrane: (0) sf daily, 984,266 sf cummulative.
- -BMI North Landfill Geocomposite: (25,000) sf daily, (675,000) sf cummulative.

o		

### **HEALTH & SAFETY**

### Entact H&S Tailgates

Safety Topic: Eastside, Day: Discussed housekeeping and dust control.

Safety Topic: CAMU, Day: Discussed housekeeping and dust control.

Eastside and CAMU, Night: Discussed driving safely on wet surfaces.

Safety Incidents: None. Dust Incidents: None.

### CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

### Daily CQA Summary.

Monitored waste relocation and waste placement from Eastside to CAMU Phase II on the night shift.

Monitored proofrolling of waste at Phase II.

Monitored waste relocation and waste placement from NW Basin/Phase IIIB to Phase II on the day shift.

Monitored subgrade preparation at Phase IIIA.

Monitored installation of geosynthetics at the North BMI Landfill.

Monitored screening operations at the 200,000 cy stockpile of 1" & 6" minus cover soils. Monitored the installation of cover soil at the North BMI Landfill.

Continue review of and updating of project documents and database to facilitate reporting.

		_	
ISSUES	AND/OR	ITEMS OF	DISCUSSION

TE VISITORS			
Name	Organization	Purpose of Visit	
		and the second s	

Report Prepared By / Title

Signature

Richard Laubinger, Construction Manager

21-Jan-09

Ver 1.1 11/07 3 of 4

# Basic Remediation Company 875 West Warm Springs Road Henderson, Nevada 89011

### **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	21-Jan-09	192
0	0	21-0411-09	192


### DAILY PHOTO LOG

Photo 1



CAMU: Phase II Daily waste placement.

Photo 2



CAMU: NW Basin/Phase IIIB trench excavation east wall showing more discolored soils to be removed

Photo 3

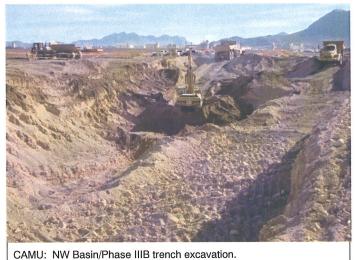


Photo 4



CAMU: Phase II Waste placement looking south.

4 of 4 Ver 1.1 11/07
