

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No. / Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	11-Mar-09	241

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Saha	rsaha@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-6660

WEATHER CONDITIONS

Conditions		Temp. (°F)	Wind	Add'l Readings
AM	Sunny/Clear	Low 41 High 64	SE 6mph	Precep. (in/hr) _____ Humidity (%) _____

Additional Weather Comments:

Calm to light winds.

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	Y
Richard Davis	Project Engineer	Construction Management Services.	Y
Chris White	Assist. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services.	Y
Kevlin Cooke	Assist. Const. Mgr	Construction Management Services.	Y
Jane Laubinger	Admin Assistant	Construction Management Services.	Y

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Sam Campbell Nelson	QA/QC Tech	Oversight	Y
Roland Derosier	QA/QC Tech	Oversight	Y
Carmon Liddell	QA/QC Tech	Oversight	Y
Jeremy Osborn	QA/QC Tech	Oversight	Y
Victor Heredia	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Becky Oano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	Y
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Elzman, ASW	Inspector	Linear Inspector	Y
Devin Gordon, McGinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	Y
Joe Ludlow, ASW	Inspector	Linear Inspector	N
Steve Morrow, ASW	Inspector	Linear Inspector	N
Brian Rakvica	Inspector	NDEP	N
PRISLI, Survey	Surveyors	Survey	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erk Geringer	Entact	Project Manager	N
Jeremy Schisler	Entact	Acting Project Manager	Y
Josh Carol	Entact	Asst Project Manager	Y
Michael Carlson	Entact	Engineer	Y
Joe Curila	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	Y
	Entact	48 Equipment Operators & Truck Drivers	Y
Ed Long	Entact	CAMU, Superintendent	Y
Lance Bruce	Entact	Health & Safety Officer	Y
Terry Harper	Entact	CAMU, Superintendent	Y
Rick McIntire	Entact	CSP, Safety	Y
Dale Walsh	Converse	CSP, Safety	N
El Blackburn	Entact	Asst Project Manager	Y
	Environmental Specialties, Inc.	1 Liner Superintendent	N
	Environmental Specialties, Inc.	12 Laborers/ Seamers	N
Carol McIntire	Entact	Health & Safety Officer	Y
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU, Mohawk Drive.	N
	Foundation Pile, Inc.	Demobilized.	N

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (9)		Eastside	-	-	-	-
CAT 324D long stick excavator		Eastside	-	-	-	-
CAT D8R Dozer with disc		Eastside	-	-	-	-
CAT 345 excavators, (6)		Eastside and CAMU	-	-	-	-
CAT 330 Excavator		CAMU	-	-	-	-
Caterpillar double pan scrapers.		Eastside, demobilized.	-	-	-	-
CAT D6 LGP Dozer (1)		Eastside	-	-	-	-
Water Trucks (2)		Eastside	-	-	-	-
JD450 Dozer		CAMU	-	-	-	-
CAT 16H Grader		CAMU	-	-	-	-
CAT D-10 Dozer		CAMU	-	-	-	-
Water Trucks (2)		CAMU	-	-	-	-
CAT D-6 Dozer, (2)		CAMU	-	-	-	-
CAT 14H Grader		CAMU	-	-	-	-
Grassall		CAMU	-	-	-	-
JLG		CAMU	-	-	-	-
IR Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Tennet Street Sweeper		Eastside and CAMU	-	-	-	-
Bomag Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Chieftain 1400 Powerscreener		Eastside, screening 1" & 6" minus	-	-	-	-
(1) Crane		Sheet pile driving. Installed. (1) Crane remains.	-	-	-	-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification	Notes
GCL	CETCO	0	rolls	For CAMU, On site	10/03/08	1298

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	11-Mar-09	241

Geocomposite	Agro	0	rolls	For CAMU, On site	2292
Geomembrane	Agro	0	rolls	For CAMU, On site	448

WORK COMPLETED

Summary of Work Completed Today

Eastside Mixing and Drying Activity:

Day Shift:

- Power screening operations layer material in the beta ditch.
- SW-7 loading out wet material and hauling to PUF-6.
- Continued pushing up previously spread material in WST ponds.
- PUD-3 completed scraping and loading out tailings from powerscreener and hauled to beta ditch.

Night Shift:

- Continued hauling material from beta ditch.
- Continued hauling material from SW-2 stockpile.

CAMU Activity:

Day Shift:

- SW-2 slit trench, excavator continued loading out trash and gravel.
- NW-3, continued loading out trash and gravel.
- RCP 42" storm drain pipe, continued pipe installation and backfill.
- NW Basin trench, scraped (8") and removed haul road to phase I from Findley property at west boundary.

Night Shift:

- Continued to place material in Phase II.

Embankment

- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

Other:

Inspections: Northwest detention basin trench, haul rd scraped 6" back to phase I. inspected and found no visible discoloration.
SW-2 slit trench, small area smoldering, trash and debris barrels with gravel.
NW-3 slit trench, small amount of trash with gravel. Viewed Montrose, DOT bags.

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I

Previous Daily Cumulative =	291,200	cy
Operations layer placed (completed) for liner certification. =	21,662	cy
Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) =	0	cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =	0	cy
To Date Phase I estimated cumulative waste placed =	291,200	cy

Phase II

Previous Daily Cumulative =	380,066	cy
Operations layer placed (completed) for liner certification. =	37,188	cy
Daily Day shift waste placed today: NW Basin to Findley property (54) loads @ 18 cy/load (2) trucks =	972	cy
Daily Day shift waste placed today: Slit Trenches, (63) loads @ 18cy/load (2) trucks =	1,134	cy
Daily Night shift placed today: (289) loads @ 18cy/load (20) trucks =	5,202	cy
To Date Phase II estimated cumulative waste placed =	387,374	cy

Phase IIIA

Previous Daily Cumulative =	21,492	cy
Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Operations layer staged in Phase IIIA for day placement (ongoing) for liner certification: (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Day shift waste placed today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Night shift waste placed today: (0) loads @ 18cy/load (0) trucks =	0	cy
To Date Phase IIIA estimated cumulative waste placed =	21,492	cy

Cummulative Total To Date All Phases =	Estimated Waste at Completion (cy)	% Complete
700,066 cy	2,050,000	34.1%

Geosynthetics Placed

Phase I (complete)	Previous	Placed	Cummulative
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	69,340	0	69,340
Phase II (complete)	Previous	Placed	Cummulative
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	520,592	0	520,592
Geotextile	0	0	0
Phase IIIA	Previous	Placed	Cummulative
GCL	221,000	0	221,000
Geomembrane	221,000	0	221,000
Geocomposite	221,000	0	221,000
Geotextile	20,000	0	20,000
Phase IIIB	Previous	Placed	Cummulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV	Previous	Placed	Cummulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V	Previous	Placed	Cummulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	11-Mar-09	241

DAILY PHOTO LOG

Photo 1




CAMU: Slit trench, NW-3.

Photo 2



CAMU: Slit trench, NW-3.

Photo 3

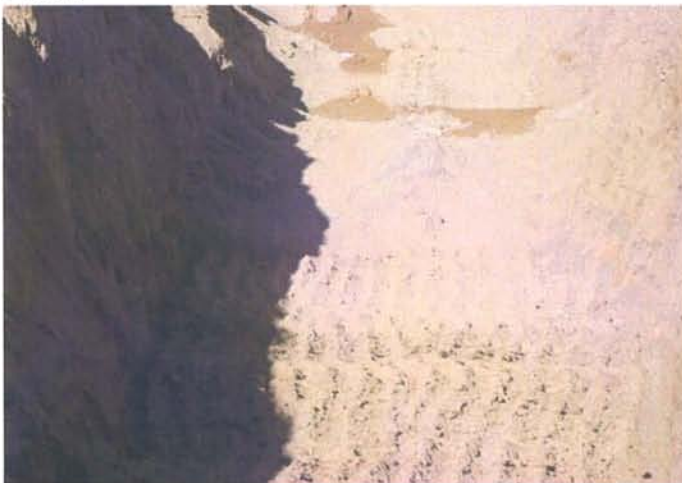

CAMU: Slit trench, NW-3.

Photo 4



CAMU: Slit trench, SW-2.
