

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	08-Sep-08	70

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu,	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (F)		Wind		Add'l Readings	
AM	Sunny / Party Cloudy	PM	Light Rain	Low	78			Precip. (in/Dy.)	
				High	103	NW	6mph	Humidity (%)	
Additional Weather Comments Calm to windy in afternoon. Light shower.									

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Dick Laubinger	Construction Manager	Construction Management Services.	Y	
Dan Brennecke	Project Manager. CM	Construction Management Services.	N	
Dave Gertz	Project Engineer	Construction Management Services.	N	
June Laubinger	Admin Assistant	Construction Management Services.	Y	
Linda Nations	Asst Const Manager	Construction Management Services	Y	

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Wayne Wofford	QA/QC Tech	Oversight	Y	
Brent Barbacane	QA/QC Tech	Oversight	Y	
Jim Cox	QA/QC Supervisor	Oversight	N	
Greg Corcoran	Engineer of Record	Oversight	N	
Rebecca Flynn	Engineer	Oversight	N	
Camon Liddell	QA/QC Tech	Oversight	N	
Dan Street	QA Manager	Oversight	Y	

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	N	
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	Y	
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Scott McKeag, McGinley	Oversight	For NDEP	N	
Devin Gordon, McGinley	Oversight	For NDEP	Y	
Dock Kim, ATC	Field Observation	For AIG	Y	
Ron Perry, ASW	Inspector	Liner Inspector	N	
PBS&J, Survey	Surveyors		N	
Brian Rakvica	Inspector	NDEP	N	

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N	
Erik Geringer	Entact	Project Manager	Y	
Josh Carrol	Entact	Asst Project Manager	Y	
Russ Karnes	Entact	Eastside, Superintendent	Y	
Michael Carlson	Entact	Engineer	Y	
Joe Curilla	Entact	Health & Safety Officer	N	
Timothy Stadt	Entact	Health and Safety Technician	Y	
	Entact	22 Equipment Operators & Truck Drivers	Y	
Ed Long	Entact	CAMU, Superintendent	Y	
	American Asphalt	Earthwork Superintendent	Y	
	American Asphalt	11 Equipment Operators & Truck Drivers,	Y	
Rick McIntire	Entact	CSP, Safety	N	
	Environmental Specialties, Inc	Liner Superintendent	N	
	Environmental Specialties, Inc	Laborers/ Seamers	N	
	Kenney Survey	CAMU	N	

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	08-Sep-08	70

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (2)		CAMU	-	-	-	-
JD D400 Dump Trucks (6)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (2)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (6)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Wagon		CAMU				-
CAT D-6 Dozer		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
Bobcat Skidsteer		CAMU				-
JLG		CAMU				-
CAT D4 dozer		CAMU				-
						-
						-
						-
						-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	QTY	UOM	Purpose	Delivery Verification			
					Condn	Qty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU				
Geocomposite	Agro	54	rolls	For CAMU				
Geomembrane	Agro	44	rolls	For CAMU				

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

- Loaded out wet soils from SW-5 with CAT 345 excavator () trucks hauled 162 loads @ 20 cy/load = 3,240 cy.
- Tractor and pans - 96 loads @ 30 cy/loads = 2,880 cy prepared material - 2 tractors.
- Watered haul Rds and Maintained them with 4,000 gal Water truck and Motorgrader.
- CAT 324 Long Stick excavator worked on bailing SW-5 soils to feed the 345 excavator for loading.
- Formed and tied rebar for the decontamination pad at Eastside.
- Continued pumping water from SC-1 to SW-12.

CAMU Activity:

Excavation

- Northwest Detention Basin excavation - 631/637 scrapers - (0) cy. 0 scraper. No activity.
- Western Ditch. Manual screening. Second lift of operations layer. Hauling and placing in Phase 1.
- Western Ditch over Phase 3A completed installation of orange construction fence. Began power screening 1" minus soils.
- Continued fence installation in Tronox property for haul road construction
- Continued placement of operations layer second lift at Phase 1.

Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy

Waste Placement

- Phase 1 estimated daily waste placed: 0 cy
- Phase 1 estimated cumulative waste placed: 0 cy
- Phase 1 Operations Layer placed daily 80 loads @ 15 cy/load, (1,200) cy, 2 trucks.

Geosynthetics.

- Phase 1 GCL placed: 0 sf daily, 347,067 sf cumulative.
- Phase 1 Geomembrane: 0 sf daily, 365,136 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 327,600 sf cumulative.
- Phase 1 Geotextile: (0) sf daily..

Other: CAMU:

Completed the installation of orange construction fence around the Phase 3A Western Ditch area. Power screening began today..

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	08-Sep-08	70

Perimeter Fence Inspection and Repair.

Southern parimeter, has several cuts. Bids in review.

HEALTH & SAFETY

Description of Health & Safety Actions Taken Today / Safety Inspections Conducted

Entact H&S Tailgates

Morning: Fire Extinguishers.

Safety Incidents: No Incidents.

QUALITY CONTROL

Description of Quality Control Actions Taken Today / Quality Inspections Conducted

Daily CQA Summary.

Inspected 12" capped haul roads for degradation. All areas ok.
Inspected/ observed operation layer placement of second lift on floor of phase 1.
Observed and documented delivery of liner. Geomembrane and Geocomposite.

Dust: Met requirements.

Deviations from CQA Plan

None

ISSUES AND/OR ITEMS OF DISCUSSION

Discussion of Issues / Concerns / Conversations / Topics

SITE VISITORS

[illegible]

Report Prepared By / Title

Date Prepared

Signature _____

Dick Laubinger, Construction Manager

8-Sep-08

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	08-Sep-08	70

DAILY PHOTO LOG

Photo 1



Eastside: Forming tying rebar setting drain sump for Decontamination Pad..

Photo 2




Eastside, Loading out wet soils SW-5 pond.

Photo 3



CAMU: Unloading liner and staging.

Photo 4

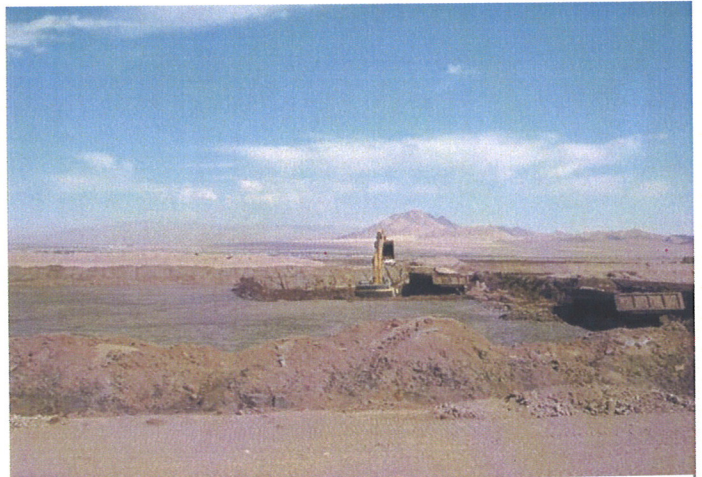

Eastside: Loading out wet soils SW-5 pond.
