

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	15-Oct-08	102

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution.com	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (°F)	Wind	Add'l Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low 53	NNE 5mph	Precip. (in/Day)	
				High 81		Humidity (%)	

Additional Weather Comments

AM 5 - 10 mph from the North, Northeast, PM, Wind same..

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Dick Laubinger	Construction Manager	Construction Management Services.	Y	
Dan Brennecke	Project Manager. CM	Construction Management Services.	Y	
Dave Goertz	Project Engineer	Construction Management Services.	N	
Richard Davis	Project Engineer	Construction Management Services.	Y	
Chris White	Assist. Const. Mgr	Construction Management Services.	Y	
	Assist. Const. Mgr	Construction Management Services.		
June Laubinger	Admin Assistant	Construction Management Services.	Y	

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Greg Corcoran	Design Engineer	Oversight	N	
Dan Street	QA Manager	Oversight	Y	
Jim Cox	QA/QC Supervisor	Oversight	N	
Robecca Flynn	Engineer	Oversight	N	
Wayne Wofford	QA/QC Tech	Oversight	Y	
Brent Barbacane	QA/QC Tech	Oversight	Y	
Camon Liddell	QA/QC Tech	Oversight	Y	

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring,	N	
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring,	Y	
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Scott McKeag, McGinley	Oversight	For NDEP	N	
Devin Gordon, McGinley	Oversight	For NDEP	Y	
Dock Kim, ATC	Field Observation	For AIG	Y	
Ron Perry, ASW	Inspector	Liner Inspector	N	
PBS&J, Survey	Surveyors	Surveying, QA	N	
Brian Rakvica	Inspector	NDEP	N	

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N	
Erik Geringer	Entact	Project Manager	Y	
Josh Carrol	Entact	Asst Project Manager	Y	
Russ Karnes	Entact	Eastside, Superintendent	Y	
Michael Carlson	Entact	Engineer	Y	
Joe Curilla	Entact	Health & Safety Officer	N	
Timothy Stadt	Entact	Health and Safety Technician	Y	
	Entact	26 Equipment Operators & Truck Drivers	Y	
Ed Long	Entact	CAMU, Superintendent	Y	
Adam Calveledge	Entact	Health & Safety Officer	Y	
Rick McIntire	Entact	CSP, Safety	Y	
	American Asphalt	1 Equipment operators	Y	
	American Asphalt	1 Superintendent	Y	
	Environmental Specialties, Inc	Liner Superintendent	N	

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	15-Oct-08	102

Environmental Specialties, Inc	Laborers/ Seamers	N	
Kenney Survey	CAMU	N	
ABC Survey	Eastside/CAMU	N	

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (2)		CAMU	-	-	-	-
JD D400 Dump Trucks (8)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (2)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (6)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Wagon		CAMU				-
CAT D-6 Dozer		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		CAMU, Phase 1				-
Tenent Street Sweeper		Eastside and CAMU				-
Bomag Smooth drum Roller		CAMU, Phase 1				-
						-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification			
					to date	Qty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU, On site		207		
Geocomposite	Agru	0	rolls	For CAMU, On site		194		
Geomembrane	Agru	0	rolls	For CAMU, On site		37		

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

- D6 dozer spread wet material over dry ponds.
- Continued pumping water from SC-1 to SW-12.
- 324 CAT excavator mixing dry soils with wet soils in dry ponds.
- Conducted dust monitoring.
- Performed decontamination of equipment.
- Electrician completed electrical installation at trailers. Waiting for poles. For final tie-in.

CAMU Activity:

Excavation ..

- Phase II continued screening soils and placing lifts on floor. Continued working on east and south slopes.
- Western ditch soils hauled into Phase 1. Day Shift: 335 loads @ 22 cy/loads = 7,370 cy (6) trucks.
- Western ditch soils hauled into Phase 1. Night Shift: 133 loads @ 22 cy/loads = 2,926 cy (4) trucks.
- Western ditch soils stockpile of 1" minus material loaded and placed in Phase 1. 82 loads @ 22cy/loads = 1,804 cy, (2) trucks.
- (2) D6 dozers placed western ditch soils in 12" lift. Followed by (2) vibratory rollers compacting (3) complete passes in Phase 1.
- Started placing operations layer on East slope of Phase 1 (1" minus soils). CAT 330 excavator used to remove Woven Geotextile.
- Conducted dust monitoring.

Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy

Waste Placement

- Phase 1 estimated daily waste placed: 335 loads @ 22cy/load = 7,370 cy
night shift placed: 215 loads @ 22cy/load = 4,730 cy
- Phase 1 estimated cumulative waste placed: 87,002 cy. Western Ditch Soils
- Phase 1 Operations Layer placed. completed. Cumulative total: 21,662

Geosynthetics. Estimated cumulative installed quantity by Phase.

- Phase 1 GCL placed: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geomembrane: 0 sf daily, 307,372 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geotextile: (0) sf daily, 69,340 sf cumulative.

Other: Work performed at Office Trailers: Electrician completed there work, waiting for Poles for final tie-in.

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	15-Oct-08	102

--

HEALTH & SAFETY

Description of Health & Safety Actions Taken Today / Safety Inspections Conducted	
1	1. Inspected the construction site for safety hazards. Found that the workers were not wearing proper safety gear (hard hats, safety glasses, and gloves). Immediate action was taken to ensure all workers were properly equipped.
2	2. Conducted a safety training session for all workers on the site. Covered topics such as fall protection, proper use of tools, and emergency procedures.
3	3. Checked the safety of the scaffolding used for the roof work. Found that some of the scaffolding was not properly secured. Repaired and reinforced the scaffolding to ensure it was safe for use.
4	4. Inspected the electrical wiring in the new addition. Found that some of the wiring was not properly insulated. Rewired the affected areas to meet safety standards.
5	5. Conducted a fire safety inspection of the building. Found that the fire extinguishers were not properly maintained. Replaced the expired extinguishers and provided fire safety training to the workers.
6	6. Inspected the safety of the construction equipment. Found that some of the equipment was not properly maintained. Scheduled maintenance for the affected equipment.
7	7. Checked the safety of the construction site during the night. Found that the site was not properly secured. Added additional security measures to ensure the site was safe during the night.
8	8. Conducted a safety inspection of the new addition. Found that the new addition was not properly secured. Added additional safety measures to ensure the new addition was safe.
9	9. Inspected the safety of the construction site during the day. Found that the workers were not wearing proper safety gear. Immediate action was taken to ensure all workers were properly equipped.
10	10. Conducted a safety training session for all workers on the site. Covered topics such as fall protection, proper use of tools, and emergency procedures.

Entact H&S Tailgates

Safety Topic Eastside: Heavy Equipment Operators, always look behind you before backing up.

Safety Topic CAMU: Evacuation procedures.

Rick McIntire, CSP on site covering for Joe Curila.

Safety Incidents: None.

Dust Incidents: None.

CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

Description of Quality Control Actions Taken Today / Quality Inspections Conducted

Daily CQA Summary..

Monitored site haul road maintenance and construction of new 12" capped haul roads.

Monitored waste relocation and placement from the western ditch into Phase 1. Monitored proof rolling. Day and Night shifts.

Monitored phase 1 slopes as woven geotextile was removed and replaced with 1" minus operations layer soils. East slope.

Monitor screening and placement as well as slope regrading of native soils in Phase II.

Sample the Beta Ditch Staging Pile complete, sample HP3 Staging Pile to date.

The first 16 Beta 1-16 samples or 80,000 cy of the beta ditch stockpile passed the solids test.

Continue updating project documents and database to facilitate reporting.

ISSUES AND/OR ITEMS OF DISCUSSION

Discussion of Issues / Concerns / Conversations / Topics

Dick Laubinger, escorted Kyle Hansen, GES to CAMU site. Pointed out areas for soil sampling. Phase 111B, Phase 4 and Phase 5. Areas. Per conversations with Ron Sahu.

SITE VISITORS

[illegible]

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Dick Laubinger, Construction Manager 15-Oct-08

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Dick Laubinger, Construction Manager 15-Oct-08

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	15-Oct-08	102

DAILY PHOTO LOG

Photo 1




CAMU: View of Phase 2 on the other side of western ditch.

Photo 2



CAMU: Phase 1 western ditch soils finishing south wall.

Photo 3

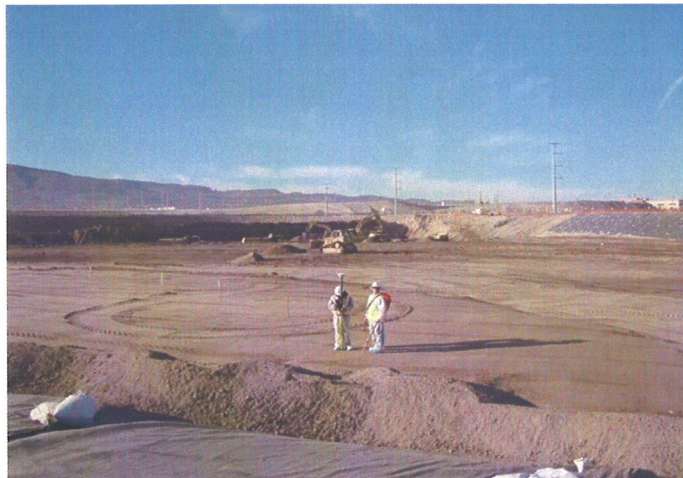

CAMU: Phase 1, Entact setting new stakes for each new lift.

Photo 4



CAMU: Phase 1 operations layer , 1" minus placed on east slope.
