

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	03-Feb-09	205

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranjit Sahu	sahuroni@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolul.com	720-641-8660

WEATHER CONDITIONS

Conditions		Temp (°)	Wind	Add'l Readings	
AM	Sunny/Clear	Low 43	High 69	Pressure (in)	Humidity (%)
PM	Sunny/Clear		10ME 5mph		
Additional Weather Comments: Calm - 5 mph.					

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	Y
Richard Davis	Project Engineer	Construction Management Services.	Y
Chris White	Asst. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Asst. Const. Mgr	Construction Management Services.	Y
Kevin Cooke	Asst. Const. Mgr	Construction Management Services.	Y
June Laubinger	Admin Assistant	Construction Management Services.	Y

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Wayne Wofford	QA/QC Tech	Oversight	N
Roland Derosier	QA/QC Tech	Oversight	Y
Camon Liddell	QA/QC Tech	Oversight	Y
Jeremy Osborn	QA/QC Tech	Oversight	Y
Victor Heredia	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	Y
Jerry Faucheux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Elzman, ASW	Inspector	Liner Inspector	Y
Devin Gordon, McGinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	Y
Joe Ludlow, ASW	Inspector	Liner Inspector	N
Steve Morrow, ASW	Inspector	Liner Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors		N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Jeremy Schissler	Entact	Acting Project Manager	Y
Josh Carol	Entact	Asst Project Manager	Y
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	Y
Ed Long	Entact	48 Equipment Operators & Truck Drivers	Y
Lance Bruce	Entact	CAMU, Superintendent	Y
Terry Harper	Entact	Health & Safety Officer	Y
Rick McIntire	Entact	CAMU, Superintendent	Y
Dale Walsh	Converse	CSP, Safety	N
El Blackburn	Entact	Asst Project Manager	Y
	Environmental Specialties, Inc	1 Liner Superintendent	Y
	Environmental Specialties, Inc	12 Laborers/ Seamers	Y
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU, Mohawk Drive.	N
	Foundation Pile, Inc.	(8) Sheet Piling Crew	Y

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (9)		Eastside	-	-	-	-
CAT 324D long stick excavator		Eastside	-	-	-	-
CAT D8R Dozer with disc		Eastside	-	-	-	-
CAT 345 excavators, (5)		Eastside and CAMU	-	-	-	-
CAT 330 Excavator		CAMU	-	-	-	-
Case double pan scrapers.		Eastside, demobilized.	-	-	-	-
CAT D6 LGP Dozer (1)		Eastside	-	-	-	-
Water Trucks (2)		Eastside	-	-	-	-
JD450 Dozer		CAMU	-	-	-	-
CAT 16H Grader		CAMU	-	-	-	-
CAT D-10 Dozer		CAMU	-	-	-	-
Water Trucks (2)		CAMU	-	-	-	-
CAT D-6 Dozer, (2)		CAMU	-	-	-	-
CAT 14H Grader		CAMU	-	-	-	-
Gradaill		CAMU	-	-	-	-
JLG		CAMU	-	-	-	-
IR Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Tenent Street Sweeper		Eastside and CAMU	-	-	-	-
Bomag Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Chieftain 1400 Powerscreener		CAMU, screening 1" & 6" minus	-	-	-	-
(2) Cranes		Sheet pile driving.	-	-	-	-

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	03-Feb-09	205

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Ultimate Verification
GCL	CETCO	9	rolls	For CAMU, On site	909
Geocomposite	Agru	108	rolls	For CAMU, On site	1101
Geomembrane	Agru	0	rolls	For CAMU, On site	258

WORK COMPLETED

Summary of Work Completed Today

Eastside Mixing and Drying Activity:

Day Shift:

- SW-2 continued mixing and drying.
- Continued pumping water from SW-7 to SW-12.
- Stockpiling material from PUA-5 for loadout with Long stick excavator.
- Excavating PUB-5 below the design excavation depth and hauling material to the Beta Ditch and SW-2.
- Working on holding tank for fire wash.

Night Shift:

- Hauled operations layer material from WST 1, 6 & 8 stockpiles.
- Continued excavating and hauling material from the Beta ditch at East end.

CAMU Activity:

Day Shift:

- Continued screening cover soils for N. BMI Landfill from berm stockpile along entrance road.
- ESI continued placing geocomposite on N. BMI Landfill.
- NW Basin/Phase IIIB excavation continued/hailed and placed in Phase II.
- Hauled 1" and 6" minus cover soils on N. BMI Landfill.
- NW-1, slit trench continued excavation/haul and placement in Phase II.
- Continued installing sheet piling.

Night Shift:

- Continued placing material in Phase II.

Embankment

- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

Other: Foundation Pile, Inc., continued installing sheet piling.

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I

Previous Daily Cumulative =	269,538 cy
Operations layer placed (completed) for liner certification, = 21,662	21,662 cy
Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) =	0 cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =	0 cy
To Date Phase I estimated cumulative waste placed =	291,200 cy

Phase II

Previous Daily Cumulative =	220,458 cy
Operations layer placed (completed) for liner certification, = 37,188	0 cy
Daily Day shift waste placed today: Phase IV,V scape,Slit Trench excavation & Phase IIIB trench excavation, (96) loads @ 20 cy/load (5 trucks) =	1,920 cy
Daily Night shift placed today: 241 loads @ 18cy/load (16 trucks) =	4,338 cy
To Date Phase II estimated cumulative waste placed =	226,716 cy

Cumulative Total To Date All Phases =	517,916 cy	Estimated Waste at Completion (cy)	% Complete
		2,200,000	23.5%

Geosynthetics Placed

	Previous Daily Cum (sf)	Placed Today (sf)	Cumulative Placed to Date (sf)
Phase I (complete)			
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	69,340	0	69,340
Phase II (complete)			
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	520,592	0	520,592
Geotextile	0	0	0
Phase IIIA			
GCL	160,000	61000	221,000
Geomembrane	160,000	61000	221,000
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IIIB			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	03-Feb-09	205

DAILY PHOTO LOG

Photo 1



CAMU: Phase IIA.

Photo 2




CAMU: Sheet Piling installation.

Photo 3



CAMU: Phase IIIB. Concrete structure.

Photo 4

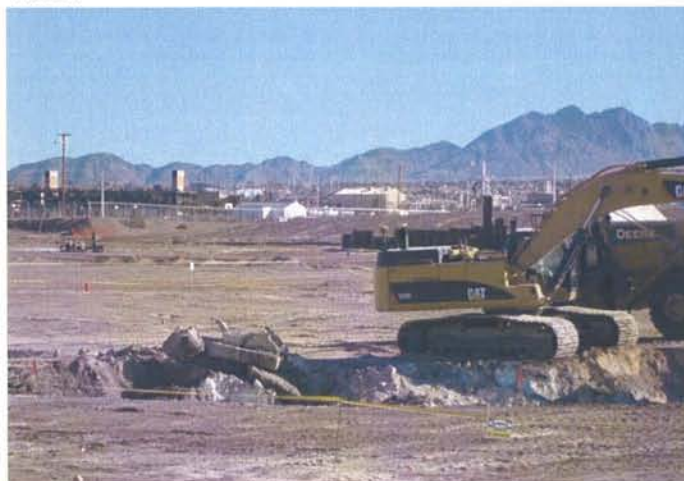

CAMU: Slit trench, NW-1.
