

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	28-Feb-09	230

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranjit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-250-5885
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-8660

WEATHER CONDITIONS

Conditions	Temp (F)	Wind	Advt Readings
AM Sunny/Clear	Low 49	High 68	Precip. in/in Humidity %
PM Sunny / Partly Cloudy		WSE 10mph	

Winds in PM 5-10 mph.

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	N
Richard Davis	Project Engineer	Construction Management Services.	N
Chris White	Asst. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Asst. Const. Mgr	Construction Management Services.	N
Kevin Cooke	Asst. Const. Mgr	Construction Management Services.	N
Jane Laubinger	Admin Assistant	Construction Management Services.	N

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Sam Campbell-Nelson	QA/QC Tech	Oversight	Y
Roland Dorosier	QA/QC Tech	Oversight	Y
Carmon Liddell	QA/QC Tech	Oversight	Y
Jeremy Osborn	QA/QC Tech	Oversight	N
Victor Heredia	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	Y
Jerry Faucheur, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Eitzman, ASW	Inspector	Unser Inspector	N
Dwain Gordon, McKinley	Oversight	For NDEP	N
Dock Kim, ATC	Field Observation	For AIG	N
Joe Ludlow, ASW	Inspector	Unser Inspector	N
Steve Morrow, ASW	Inspector	Unser Inspector	N
Brian Plakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Survey	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Jeremy Schlusser	Entact	Acting Project Manager	Y
Josh Carol	Entact	Asst Project Manager	Y
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadl	Entact	Health and Safety Technician	Y
Ed Long	Entact	48 Equipment Operators & Truck Drivers	Y
Lance Bruce	Entact	CAMU, Superintendent	N
Terry Harper	Entact	Health & Safety Officer	N
Rick McInire	Entact	CAMU, Superintendent	N
Dale Walsh	Converse	CSP, Safety	N
Ell Blackburn	Entact	CSP, Safety	Y
	Environmental Specialties, Inc	Asst Project Manager	N
	Environmental Specialties, Inc	1 Liner Superintendent	N
		12 Laborers/ Seamers	N
Carol McInire	Entact	Health & Safety Officer	N
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU, Mohawk Drive.	N
	Foundation Pile, Inc.	Demobilized.	N

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No	Work Performed			
CAT D400E Dump Truck (10)		CAMU	-	-	-
JD D400 Dump Trucks (8)		Eastside	-	-	-
CAT 324D long stick excavator		Eastside	-	-	-
CAT D6R Dozer with disc		Eastside	-	-	-
CAT 345 excavators, (5)		Eastside and CAMU	-	-	-
CAT 330 Excavator		CAMU	-	-	-
Casa double pan scrapers.		Eastside, demobilized.	-	-	-
CAT D6 LGP Dozer (1)		Eastside	-	-	-
Water Trucks (2)		Eastside	-	-	-
JD450 Dozer		CAMU	-	-	-
CAT 16H Grader		CAMU	-	-	-
CAT D-10 Dozer		CAMU	-	-	-
Water Trucks (2)		CAMU	-	-	-
CAT D-6 Dozer, (2)		CAMU	-	-	-
CAT 14H Grader		CAMU	-	-	-
Grapple		CAMU	-	-	-
JLG		CAMU	-	-	-
IR Smooth drum Roller		CAMU, Phase 1	-	-	-
Tenent Street Sweeper		Eastside and CAMU	-	-	-
Bomag Smooth drum Roller		CAMU, Phase 1	-	-	-
Chieftain 1400 Powerscreener		Eastside, screening 1" & 6" minus	-	-	-
(1) Crane		Sheet pile driving. Installed, (1) Crane remains.	-	-	-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOI	Purpose	Inventory Verification
GCL	CEICO	0	rolls	For CAMU, On site	1091

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No. / Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	28-Feb-09	230

Geocomposite	Agro	0	rolls	For CAMU, On site	2292
Geomembrane	Agro	0	rolls	For CAMU, On site	448

WORK COMPLETED

Interim Final Inspection Table

Eastside Mixing and Drying Activity:

Day Shift:

- PUC-3 remediation of north berm south face to vertical, also scraping top of berm.
- PUD-4, continue screening for operations layer.
- SW-2 continue mixing materials
- HP-2, stockpiling material for loadout with longstick excavator.

Night Shift:

- No Activity.

CAMU Activity:

Day Shift:

- Continued grading N. BMI Landfill.
- Continued excavating NW-2, waste continues to be trash and paper products. Activated pyrophoric substances, periodically.
- Continued excavating NW-3 second excavator, waste consists of gravel and debris.
- Continued the installation of 42" RCP storm drain system.
- Phase IIIA, continued placing operations layer.

Night Shift:

- No Activity.

Embankment

- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

Other:

Inspections: Silt trenches, NW-2, Waste continues to be trash and paper products with soils. Also pyrophoric substances, periodically.
NW-3, Waste continued to be debris and gravel.

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I

Previous Daily Cumulative =	291,200	cy
Operations layer placed (completed) for liner certification. = 21,662	0	cy
Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) =	0	cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =	0	cy
To Date Phase I estimated cumulative waste placed =	291,200	cy

Phase II

Previous Daily Cumulative =	331,664	cy
Operations layer placed (completed) for liner certification. = 37,188	0	cy
Daily Day shift waste placed today: Phase IIIB (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Day shift waste placed today: Silt Trenches, (49) loads @ 18cy/load (3) trucks =	882	cy
Daily Night shift placed today: (0) loads @ 18cy/load (0) trucks =	0	cy
To Date Phase II estimated cumulative waste placed =	332,546	cy

Phase IIIA

Previous Daily Cumulative =	11,862	cy
Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Operations layer staged in Phase IIIA for day placement (ongoing) for liner certification: (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Day shift waste placed today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Night shift waste placed today: (0) loads @ 18cy/load (0) trucks =	0	cy
To Date Phase IIIA estimated cumulative waste placed =	11,862	cy

Cumulative Total To Date All Phases =	Estimated Waste at Completion (cy)	% Complete
635,608 cy	2,050,000	31.0%

Geosynthetics Placed

Phase I (complete)	Previous	Placed	Cumulative
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	69,340	0	69,340
Phase II (complete)	Previous	Placed	Cumulative
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	520,592	0	520,592
Geotextile	0	0	0
Phase IIIA	Previous	Placed	Cumulative
GCL	221,000	0	221,000
Geomembrane	221,000	0	221,000
Geocomposite	221,000	0	221,000
Geotextile	20,000	0	20,000
Phase IIIB	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	28-Feb-09	230

DAILY PHOTO LOG

Photo 1




Eastside: PUC-3, Remediating Northern berm.

Photo 2



Eastside: PUA-8

Photo 3

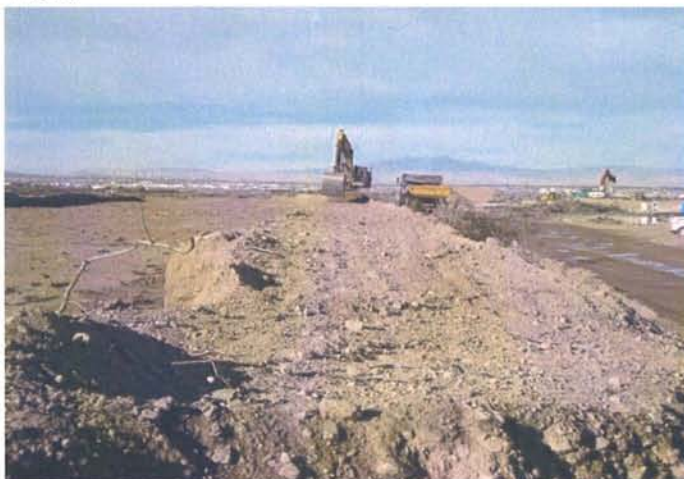

Eastside: PUC-3. North berm.

Photo 4



CAMU: RCP storm drain pipe installation.
