

### DAILY PRODUCTION & QUALITY CONTROL REPORT

| Project No./Contract No. | Project Title / Location                    | Day of Report | Report No. |
|--------------------------|---------------------------------------------|---------------|------------|
| 6389                     | BRC Eastside Common Areas Soils Remediation | 25-Mar-09     | 255        |

#### PROJECT POINTS OF CONTACT

| Position               | Name              | E-Mail Address                        | Phone No.    |
|------------------------|-------------------|---------------------------------------|--------------|
| BRC PROJECT MANAGER    | Lee Faris         | lfaris@landwellco.com                 | 702-567-0400 |
| BRC PROJECT MANAGER    | Raeel Sahu        | rsahu@earthlink.net                   | 702-567-0400 |
| CONIST PROJECT MANAGER | Dan Brennecke     | Dan.Brennecke@westonsolutions.com     | 970-290-5888 |
| Construction Manager   | Richard Laubinger | Richard.Laubinger@westonsolutions.com | 720-641-8660 |

#### WEATHER CONDITIONS

| Conditions                | Temp (°F)         | Wind    | Add'l Readings                   |
|---------------------------|-------------------|---------|----------------------------------|
| All Sunny / Partly Cloudy | Low 48<br>High 67 | W 10mph | Precip. (inches)<br>Humidity (%) |

Actual Weather Conditions

Light wind to 9 mph.

#### ON-SITE WESTON PERSONNEL

| Name           | Position             | Trade / Work Performed           | Y/N |
|----------------|----------------------|----------------------------------|-----|
| Dick Laubinger | Construction Manager | Construction Management Services | Y   |
| Dan Brennecke  | Project Manager, CM  | Construction Management Services | N   |
| Richard Davis  | Project Engineer     | Construction Management Services | Y   |
| Chris White    | Asst. Const. Mgr     | Construction Management Services | Y   |
| Wayne Hodgson  | Asst. Const. Mgr     | Construction Management Services | Y   |
| Kevin Cooke    | Asst. Const. Mgr     | Construction Management Services | Y   |
| June Laubinger | Admin Assistant      | Construction Management Services | Y   |
|                |                      |                                  |     |
|                |                      |                                  |     |
|                |                      |                                  |     |

#### ON-SITE GEOSYNTEC PERSONNEL

| Name                | Position         | Trade / Work Performed | Y/N |
|---------------------|------------------|------------------------|-----|
| Greg Corcoran       | Design Engineer  | Oversight              | Y   |
| Dan Street          | QA Manager       | Oversight              | Y   |
| Jim Cox             | QA/QC Supervisor | Oversight              | N   |
| Rebecca Flynn       | Engineer         | Oversight              | N   |
| Sam Campbell-Nelson | QA/QC Tech       | Oversight              | Y   |
| Roland Derosier     | QA/QC Tech       | Oversight              | Y   |
| Camron Liddell      | QA/QC Tech       | Oversight              | Y   |
| Victor Heredia      | QA/QC Tech       | Oversight              | Y   |

#### ON-SITE SUPPORT PERSONNEL

| Name                        | Position                  | Trade / Work Performed | Y/N |
|-----------------------------|---------------------------|------------------------|-----|
| Doug Herlocker, Tetra Tech  | Air Monitoring Specialist | Air Monitoring         | N   |
| Bocky Dano, Tetra Tech      | Air Monitoring Specialist | Air Monitoring         | Y   |
| Jerry Fauschoux, Tetra Tech | Air Monitoring Specialist | Air Monitoring         | N   |
|                             |                           |                        |     |
|                             |                           |                        |     |

#### OVERSITE PERSONNEL

| Name                   | Position          | Trade / Work Performed | Y/N |
|------------------------|-------------------|------------------------|-----|
| Mark Elzman, ASW       | Inspector         | Liner Inspector        | Y   |
| Devin Gordon, McGinley | Oversight         | For NDEP               | Y   |
| Dock Kim, ATC          | Field Observation | For AIG                | Y   |
| Joe Ludow, ASW         | Inspector         | Liner Inspector        | N   |
| Steve Morrow, ASW      | Inspector         | Liner Inspector        | N   |
| Brian Rakvica          | Inspector         | NDEP                   | N   |
| PBS&J, Survey          | Surveyors         | Survey                 | N   |

#### ON-SITE CONTRACTOR PERSONNEL

| Name            | Company                        | Trade / Work Performed                 | Y/N |
|-----------------|--------------------------------|----------------------------------------|-----|
| Erk Geringer    | Entact                         | Project Manager                        | N   |
| Jeremy Schaefer | Entact                         | Acting Project Manager                 | Y   |
| Josh Carol      | Entact                         | Asst Project Manager                   | Y   |
| Michael Carlson | Entact                         | Engineer                               | Y   |
| Joe Curilla     | Entact                         | Health & Safety Officer                | N   |
| Timothy Stadt   | Entact                         | Health and Safety Technician           | Y   |
| Ed Long         | Entact                         | 48 Equipment Operators & Truck Drivers | Y   |
| Lance Bruce     | Entact                         | CAMU, Superintendent                   | Y   |
| Terry Harper    | Entact                         | Health & Safety Officer                | Y   |
| Rick McIntire   | Entact                         | CAMU, Superintendent                   | Y   |
| Dale Walsh      | Converse                       | CSP, Safety                            | N   |
| El Blackburn    | Entact                         | Asst Project Manager                   | Y   |
|                 | Environmental Specialties, Inc | 1 Liner Superintendent                 | N   |
|                 | Environmental Specialties, Inc | 12 Laborers/ Seamers                   | N   |
| Carol McIntire  | Entact                         | Health & Safety Officer                | Y   |
| Roger Wagner    | Entact                         | Eastside, Superintendent, Night Shift. | Y   |
|                 | ABC Survey                     | Eastside/CAMU                          | N   |
|                 | Foundation Pile, Inc.          | Demobilized.                           | N   |
|                 |                                |                                        |     |
|                 |                                |                                        |     |

#### ON-SITE EQUIPMENT

| Equipment                     | Vendor / Tag No. | Work Performed                                   |   |   |   |   |
|-------------------------------|------------------|--------------------------------------------------|---|---|---|---|
| CAT D400E Dump Truck (10)     |                  | CAMU                                             | - | - | - | - |
| JD D400 Dump Trucks (9)       |                  | Eastside                                         | - | - | - | - |
| CAT 320D long stick excavator |                  | Eastside                                         | - | - | - | - |
| CAT D6R Dozer with disc       |                  | Eastside                                         | - | - | - | - |
| CAT 345 excavators, (5)       |                  | Eastside and CAMU                                | - | - | - | - |
| CAT 330 Excavator             |                  | CAMU                                             | - | - | - | - |
| Case double pan scrapers.     |                  | Eastside, demobilized.                           | - | - | - | - |
| CAT D6 LGP Dozer (1)          |                  | Eastside                                         | - | - | - | - |
| Water Trucks (2)              |                  | Eastside                                         | - | - | - | - |
| JD450 Dozer                   |                  | CAMU                                             | - | - | - | - |
| CAT 16H Grader                |                  | CAMU                                             | - | - | - | - |
| CAT D-10 Dozer                |                  | CAMU                                             | - | - | - | - |
| Water Trucks (3)              |                  | CAMU                                             | - | - | - | - |
| CAT D-6 Dozer, (3)            |                  | CAMU                                             | - | - | - | - |
| CAT 14H Grader                |                  | CAMU                                             | - | - | - | - |
| Gradall                       |                  | CAMU                                             | - | - | - | - |
| JLG                           |                  | CAMU                                             | - | - | - | - |
| IR Smooth drum Roller         |                  | CAMU, Phase 1                                    | - | - | - | - |
| Tonnet Street Sweeper         |                  | Eastside and CAMU                                | - | - | - | - |
| Bomg Smooth drum Roller       |                  | CAMU, Phase 1                                    | - | - | - | - |
| Cherlain 1400 Powerscreener   |                  | CAMU, screening 1" & 6" minus                    | - | - | - | - |
| (1) Crane                     |                  | Sheet pile driving. Installed, (1)Crane remains. | - | - | - | - |
|                               |                  |                                                  |   |   |   |   |
|                               |                  |                                                  |   |   |   |   |

#### MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

| Material | Vendor | Today | UOM   | Purpose           | Delivery Vehicle(s) |
|----------|--------|-------|-------|-------------------|---------------------|
| GCL      | CETCO  | 0     | rolls | For CAMU, On site | 1288                |

# DAILY PRODUCTION & QUALITY CONTROL REPORT

| Project No./Contract No. | Project Title / Location                    | Day of Report | Report No. |
|--------------------------|---------------------------------------------|---------------|------------|
| 6389                     | BRC Eastside Common Areas Soils Remediation | 25-Mar-09     | 255        |

|              |      |    |       |                   |      |  |
|--------------|------|----|-------|-------------------|------|--|
| Geocomposite | Agro | 0  | rolls | For CAMU, On site | 2373 |  |
| Geomembrane  | Agro | 44 | rolls | For CAMU, On site | 514  |  |

## WORK COMPLETED

Description of Work Completed Today

### Eastside Mixing and Drying Activity:

#### Day Shift:

- Continued final scrape in PUA-7, hauled material to SW-2.
- Continued hauling and spreading wet material from SW-7 to SW-5.
- Continued mixing and stockpiling material in SW-2.
- Farming wet material that has been spread out to dry with the D8 dozer and disc.
- Began building haul rd to north end of beta ditch.

#### Night Shift:

- Hauling and placing material from the Beta ditch and HP-3, SW-2 stockpiles into Phase II.

### CAMU Activity:

#### Day Shift:

- Continued excavating east end of Silt trench, NW-1, loading and hauling white/gray and gravel material to Phase II.
- Continued excavating to the east in Silt trench, SW-2, loading and hauling trash and gravel to Phase II.
- Continued screening 1" and 6" soils stockpiling in berm along entrance haul rd.
- Continued hauling and placing 6" minus soils to BMI North.
- Worked on RCP pipe system, manhole preparation.
- Phase IIIB trench continued excavating east from concrete wall. Haul and placed in Phase II.
- Phase I LCRS measured. Phase I Vadose pump installed. Phase II LCRS measured and pumped.

#### Night Shift:

- Place waste in Phase II.

### Embankment

- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

### Sump/Vadose Monitoring:

- Phase I: LCRS Sump: Measurement taken (2.80).
- Vadose: Measurement taken, N/A. Not measured due to new pump being installed.
- Phase II: LCRS Sump: Measurement taken, (1.20). Water pumped: approx. 4,000 gallons.
- Vadose: Reported dry by Entact.

### Inspections:

- CAMU: NW-1, continued east, encountering white/gray with gravel material.
- SW-2, continued east, encountering trash and gravel material.
- Phase IIIB, trench excavation, east from concrete wall. White/gray soils and concrete, mixed.

Eastside: Weston monitored PUA-7 scrape.

## Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

### Phase I

|                                                                                                                        |                |           |
|------------------------------------------------------------------------------------------------------------------------|----------------|-----------|
| Previous Daily Cumulative =                                                                                            | 291,200        | cy        |
| Operations layer placed (completed) for liner certification. =                                                         | 21,662         | cy        |
| Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) = | 0              | cy        |
| Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =                                                       | 0              | cy        |
| <b>To Date Phase I estimated cumulative waste placed =</b>                                                             | <b>291,200</b> | <b>cy</b> |

### Phase II

|                                                                                                     |                |           |
|-----------------------------------------------------------------------------------------------------|----------------|-----------|
| Previous Daily Cumulative =                                                                         | 465,926        | cy        |
| Operations layer placed (completed) for liner certification. =                                      | 37,188         | cy        |
| Daily Day shift waste placed today: NW Basin/Phase IIIB trench (60) loads @ 18 cy/load (2) trucks = | 1,080          | cy        |
| Daily Day shift waste placed today: Silt Trenches, (99) loads @ 18cy/load (4) trucks =              | 1,782          | cy        |
| Daily Night shift placed today: (314) loads @ 18cy/load (20) trucks =                               | 5,652          | cy        |
| <b>To Date Phase II estimated cumulative waste placed =</b>                                         | <b>474,440</b> | <b>cy</b> |

### Phase IIIA

|                                                                                                                                |               |           |
|--------------------------------------------------------------------------------------------------------------------------------|---------------|-----------|
| Previous Daily Cumulative =                                                                                                    | 21,492        | cy        |
| Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks =                                      | 0             | cy        |
| Operations layer staged in Phase IIIA for day placement (ongoing) for liner certification: (0) loads @ 18 cy/load (0) trucks = | 0             | cy        |
| Daily Day shift waste placed today: (0) loads @ 18 cy/load (0) trucks =                                                        | 0             | cy        |
| Daily Night shift waste placed today: (0) loads @ 18cy/load (0) trucks =                                                       | 0             | cy        |
| <b>To Date Phase IIIA estimated cumulative waste placed =</b>                                                                  | <b>21,492</b> | <b>cy</b> |

|                                              |                |           |                                           |                  |                   |              |
|----------------------------------------------|----------------|-----------|-------------------------------------------|------------------|-------------------|--------------|
| <b>Cumulative Total To Date All Phases =</b> | <b>787,132</b> | <b>cy</b> | <b>Estimated Waste at Completion (cy)</b> | <b>2,050,000</b> | <b>% Complete</b> | <b>38.4%</b> |
|----------------------------------------------|----------------|-----------|-------------------------------------------|------------------|-------------------|--------------|

## Geosynthetics Placed

| Phase I (complete)  | Previous | Placed | Cumulative |
|---------------------|----------|--------|------------|
| GCL                 | 307,372  | 0      | 307,372    |
| Geomembrane         | 307,372  | 0      | 307,372    |
| Geocomposite        | 307,372  | 0      | 307,372    |
| Geotextile          | 69,340   | 0      | 69,340     |
| Phase II (complete) | Previous | Placed | Cumulative |
| GCL                 | 498,468  | 0      | 498,468    |
| Geomembrane         | 498,468  | 0      | 498,468    |
| Geocomposite        | 520,592  | 0      | 520,592    |
| Geotextile          | 0        | 0      | 0          |
| Phase IIIA          | Previous | Placed | Cumulative |
| GCL                 | 221,000  | 0      | 221,000    |
| Geomembrane         | 221,000  | 0      | 221,000    |
| Geocomposite        | 221,000  | 0      | 221,000    |
| Geotextile          | 20,000   | 0      | 20,000     |
| Phase IIIB          | Previous | Placed | Cumulative |
| GCL                 | 0        | 0      | 0          |
| Geomembrane         | 0        | 0      | 0          |
| Geocomposite        | 0        | 0      | 0          |
| Geotextile          | 0        | 0      | 0          |
| Phase IV            | Previous | Placed | Cumulative |
| GCL                 | 0        | 0      | 0          |
| Geomembrane         | 0        | 0      | 0          |
| Geocomposite        | 0        | 0      | 0          |
| Geotextile          | 0        | 0      | 0          |
| Phase V             | Previous | Placed | Cumulative |
| GCL                 | 0        | 0      | 0          |
| Geomembrane         | 0        | 0      | 0          |
| Geocomposite        | 0        | 0      | 0          |
| Geotextile          | 0        | 0      | 0          |



## Basic Remediation Company

875 West Warm Springs Road  
Henderson, Nevada 89011

### DAILY PRODUCTION & QUALITY CONTROL REPORT

| Project No./Contract No. | Project Title / Location                         | Day of Report | Report No. |
|--------------------------|--------------------------------------------------|---------------|------------|
| 6389<br>0                | BRC Eastside Common Areas Soils Remediation<br>0 | 25-Mar-09     | 255        |

### DAILY PHOTO LOG

Photo 1




CAMU: Off loading geosynthetics.

Photo 2




CAMU: Phase I North slope.

Photo 3

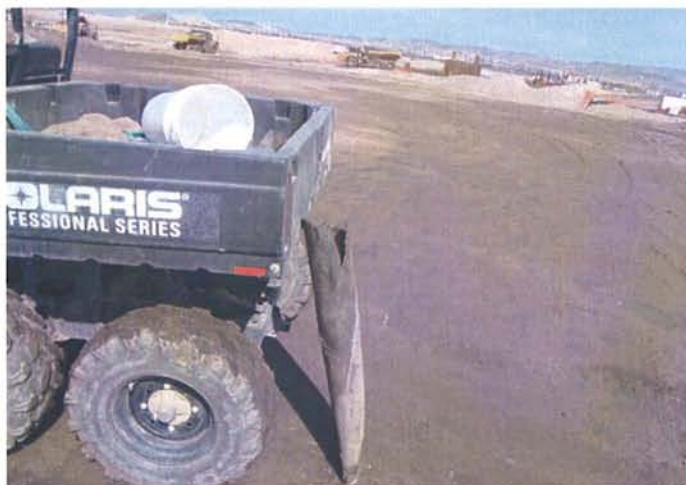

CAMU: Phase I,

Photo 4

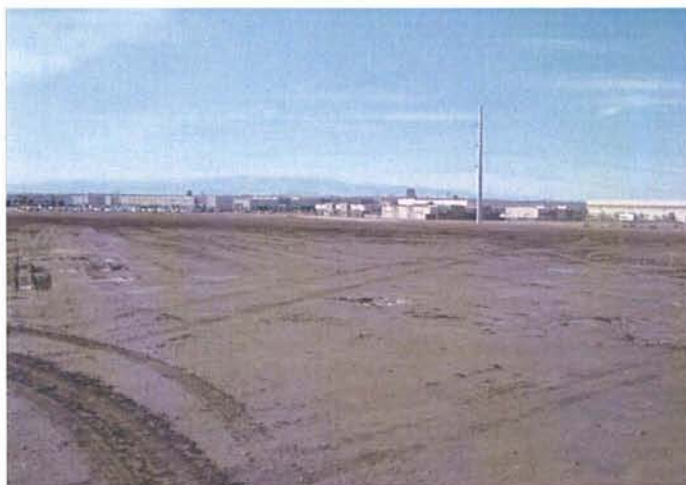

CAMU: Phase I.
