

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No. / Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	04-Apr-09	265

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	farris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranjit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-8660

WEATHER CONDITIONS

Conditions		Temp. (°F)		Wind	Additional Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low 38	High 65	Wind 10 mph
Relative Humidity: 30%						
Calm to 10 mph.						

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	N
Richard Davis	Project Engineer	Construction Management Services.	N
Chris White	Asst. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Asst. Const. Mgr	Construction Management Services.	Y
Kevin Cooke	Asst. Const. Mgr	Construction Management Services.	Y
June Laubinger	Admin Assistant	Construction Management Services.	N

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Grog Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Sam Campbell Nelson	QA/QC Tech	Oversight	Y
Roland Drouler	QA/QC Tech	Oversight	Y
Camron Liddell	QA/QC Tech	Oversight	N
Victor Heredia	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Bocky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	Y
Jerry Fauscheux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Eizman, ASW	Inspector	Liner Inspector	N
Devlin Gordon, McKinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIA	N
Joe Ludlow, ASW	Inspector	Liner Inspector	N
Steve Morrow, ASW	Inspector	Liner Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Survey	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erk Geringer	Entact	Project Manager	N
Jeremy Schlöser	Entact	Acting Project Manager	Y
Josh Carrol	Entact	Asst Project Manager	N
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	N
Ed Long	Entact	40 Equipment Operators & Truck Drivers	Y
Lance Bruce	Entact	CAMU, Superintendent	Y
Terry Harper	Entact	CAMU, Superintendent	Y
Rick McIntire	Entact	CSP, Safety	N
Dale Walsh	Converse	CSP, Safety	N
Eli Blackburn	Entact	Asst Project Manager	Y
	Environmental Specialties, Inc	1 Liner Superintendent	N
	Environmental Specialties, Inc	12 Laborers/ Seamers	N
Carol McIntire	Entact	Health & Safety Officer	Y
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU	N
	Foundation Pile, Inc.	Demobilized.	N

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed	Y/N
CAT D80E Dump Truck (10)		CAMU	Y
JD D400 Dump Trucks (9)		Eastside	Y
CAT 324D long stick excavator		Eastside	Y
CAT D8H Dozer with disc		Eastside	Y
CAT 345 excavators, (6)		Eastside and CAMU	Y
CAT 330 Excavator		CAMU	Y
Case double pan scrapers.		Eastside, demobilized	Y
CAT D6 LGP Dozer (1)		Eastside	Y
Water Trucks (2)		Eastside	Y
30450 Dozer		CAMU	Y
CAT 16H Grader		CAMU	Y
CAT D-10 Dozer		CAMU	Y
Water Trucks (3)		CAMU	Y
CAT D-6 Dozer, (3)		CAMU	Y
CAT 14H Grader		CAMU	Y
Grapple		CAMU	Y
JLG		CAMU	Y
IR Smooth drum Roller		CAMU, Phase 1	Y
Tenent Street Sweeper		Eastside and CAMU	Y
Bomag Smooth drum Roller		CAMU, Phase 1	Y
Chieftain 1400 Powerscreeper		CAMU	Y
(1) Crane		Sheet pile driving. Installed, (1)Crane remains.	Y

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification
GCL	CETCO	13	rolls	For CAMU, On site	1574

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No. / Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	04-Apr-09	265

Geocomposite	Agro	0	rolls	For CAMU, On site	23/3
Geomembrane	Agro	0	rolls	For CAMU, On site	514

WORK COMPLETED

Summary of Work Completed Today

Eastside Mixing and Drying Activity

Day Shift:

- Excavating/scraping haul rd North of PUA-4, hauling material to HP-2, SW-10.
- Excavating/scraping floor of PUA-8, hauling material to beta ditch.
- Excavating/loading out wet material from SW-7 hauling to WST-5 and CTR-3.
- Farming wet material that has been spread out on dry pond with D8 and disc.

Night Shift:

- Hauled material from Beta ditch, HP-2 and SW-4 to Phase IIIA.

CAMU Activity

Day Shift:

- Continued and completed backfilling and compacting trench on Findley property. Converse present to monitor and test.
- Continued cutting ties in Phase II.
- Phase I LCRS measured. Phase I Vadose measured. Phase II LCRS measured and pumped.
- Continued installing new haul rd into Phase IIIA and II.
- Offloaded trucks of geosynthetics delivered.

Night Shift:

- Placed material in Phase II and Phase IIIA.

Embankment

- Phase I embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

Sump/Vadose Monitoring

Phase I: LCRS Sump: Measurement taken: 8AM. (2.00). Water Pumped: N/A.
Vadose: Measurement taken: 8AM. (0.67). Water Pumped: N/A.
Phase II: LCRS Sump: Measurement taken: 8AM. (2.70). Water Pumped: 688 gallons.
Vadose: N/A.

Inspections: CAMU:

Weston monitored sump access.
Inspected SW-2 slit trench, found (2) areas on North slope needing more attention. Also noted black asphaltic material at the base of (3) sheet piling.

Eastside: Perimeter fence inspected: (2) openings found over the weekend, temporarily repaired. Final repair to be 4-6-09

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I

Previous Daily Cumulative = 291,200 cy
Operations layer placed (completed) for liner certification. = 21,662 0 cy
Daily Day shift waste placed today: Phase IV/V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) = 0 cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) = 0 cy
To Date Phase I estimated cumulative waste placed = 291,200 cy

Phase II

Previous Daily Cumulative = 493,002 cy
Operations layer placed (completed) for liner certification. = 37,188 cy
Daily Day shift waste placed today: NW Basin/Phase IIIB trench (0) loads @ 18 cy/load (0) trucks = 0 cy
Daily Day shift waste placed today: Silt Trenches, (0) loads @ 18cy/load (0) trucks = 0 cy
Daily Night shift placed today: (0) loads @ 18cy/load (0) trucks = 0 cy
To Date Phase II estimated cumulative waste placed = 493,002 cy

Phase IIIA

Previous Daily Cumulative = 36,036 cy
Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks = 0 cy
Operations layer placed (completed for liner certification = 21,276 0 cy
Daily Day shift waste placed today: (0) loads @ 18 cy/load (0) trucks = 0 cy
Daily Night shift waste placed today: (268) loads @ 18cy/load (18) trucks = 4,824 cy
To Date Phase IIIA estimated cumulative waste placed = 40,860 cy

Cummulative Total To Date All Phases = 825,062 cy
Estimated Waste at Completion (cy) 2,050,000
% Complete 40.2%

Geosynthetics Placed

Phase I (complete)	Previous	Placed	Cummulative
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	69,340	0	69,340
Phase II (complete)			
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	528,592	0	528,592
Geotextile	0	0	0
Phase IIIA			
GCL	221,000	0	221,000
Geomembrane	221,000	0	221,000
Geocomposite	221,000	0	221,000
Geotextile	20,000	0	20,000
Phase IIIB			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	04-Apr-09	265


DAILY PHOTO LOG

Photo 1



CAMU: Findley Property backfill and compaction.

Photo 2

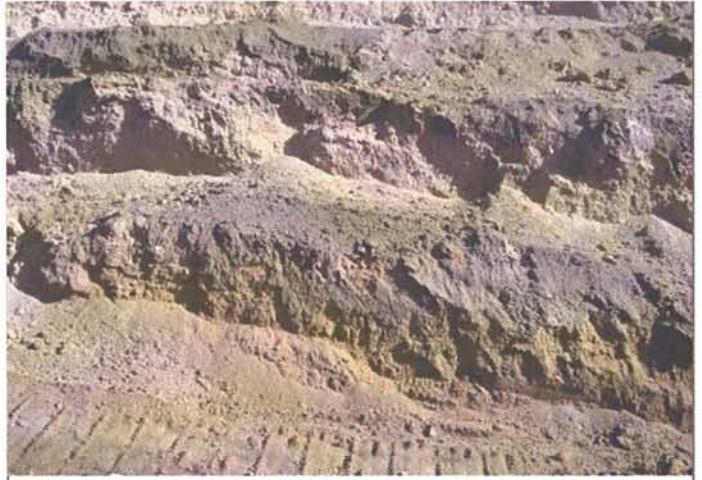

CAMU: SW-2, Slit trench inspection, area identified for additional excavation.

Photo 3



CAMU: SW-2, slit trench, area identified for additional attention.

Photo 4



CAMU: SW-2, Slit trench excavation.
