

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	18-Jan-09	189

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.c	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (°F)	Wind	Add'l Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low 40		Precip. (in/hr)	
				High 42	W 5mph	Humidity (%)	
Additional Weather Comments Light wind. Clear Night.							

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Dick Laubinger	Construction Manager	Construction Management Services.	N	
Dan Brennecke	Project Manager. CM	Construction Management Services.	N	
Richard Davis	Project Engineer	Construction Management Services.	N	
Chris White	Assist. Const. Mgr	Construction Management Services.	N	
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services.	Y	
Kevin Cooke	Assist. Const. Mgr	Construction Management Services.	Y	
June Laubinger	Admin Assistant	Construction Management Services.	N	

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Greg Corcoran	Design Engineer	Oversight	N	
Dan Street	QA Manager	Oversight	N	
Jim Cox	QA/QC Supervisor	Oversight	N	
Robecca Flynn	Engineer	Oversight	N	
Wayne Wofford	QA/QC Tech	Oversight	N	
Roland Derosier	QA/QC Tech	Oversight	N	
Camon Liddell	QA/QC Tech	Oversight	N	
Jeremy Osborn	QA/QC Tech	Oversight	Y	
Victor Heredia	QA/QC Tech	Oversight	N	

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	N	
Jerry Faucheux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N	
Mark Eizman, ASW	Inspector	Liner Inspector	N	
Devin Gordon, McGinley	Oversight	For NDEP	N	
Dock Kim, ATC	Field Observation	For AIG	N	
Joe Ludlow, ASW	Inspector	Liner Inspector	N	
Steve Morrow, ASW	Inspector	Liner Inspector	N	
Brian Rakvica	Inspector	NDEP	N	
PBS&J, Survey	Surveyors	Surveying, QA	N	

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N	
Erik Geringer	Entact	Project Manager	N	
Josh Carrol	Entact	Asst Project Manager	N	
Russ Karnes	Entact	Eastside, Superintendent	N	
Michael Carlson	Entact	Engineer	N	
Joe Curilla	Entact	Health & Safety Officer	Y	
Timothy Stadt	Entact	Health and Safety Technician	N	
	Entact	26 Equipment Operators & Truck Drivers	Y	
Ed Long	Entact	CAMU, Superintendent	N	
Lance Bruce	Entact	Health & Safety Officer	Y	
Terry Harper	Entact	CAMU, Superintendent	Y	
Rick McIntire	Entact	CSP, Safety	N	
Dale Walsh	Converse	CSP, Safety	N	

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	18-Jan-09	189

Eli Blackburn	Entact	Asst Project Manager	N	
	Environmental Specialties, Inc	1 Liner Superintendent	N	
	Environmental Specialties, Inc	12 Laborers/ Seamers	N	
	Kenney Survey	CAMU	N	
	ABC Survey	Eastside/CAMU, Mohawk Drive.	N	

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (9)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator, (3)		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside, demobilized.		-	-	-
CAT D6 LGP Dozer (1)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (2)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Trucks (2)		CAMU				-
CAT D-6 Dozer, (2)		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		CAMU, Phase 1				-
Tenent Street Sweeper		Eastside and CAMU				-
Bomag Smooth drum Roller		CAMU, Phase 1				-
Chieftain 1400 Powerscreener		CAMU, screening 1" & 6" minus				-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification			
					to date	Qty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU, On site		830		
Geocomposite	Agro	0	rolls	For CAMU, On site		886		
Geomembrane	Agro	0	rolls	For CAMU, On site		258		

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

Day Shift:

- No Activity.

Night Shift:

- Continued hauling material from HP-3/HP-2 and PUA-4.

CAMU Activity:

Day Shift:

- No Activity.

Night Shift:

- Continued placing waste in Phase II.

Embankment

- Phase 1 embankment, complete.

- Phase 1 estimated cumulative embankment placed: 0 cy

- Phase II embankment, complete.

Waste Placement

- Phase 1 estimated daily waste placed, (Phase IIIB Trench): 0 loads @ 20 cy/load = 0 cy. (0 trucks).

night shift placed: (0) loads @ 18cy/load = 0 cy.

- Phase 1 estimated cumulative waste placed: 291,020 cy.

- Phase 1 Operations Layer placed. completed. Cumulative total: 21,662

- Phase 2 estimated night shift placed: 294 loads @ 18cy/load = 5,292 cy, (19 trucks).

- Phase 2 estimated day shift placed: 0 loads @ 20 cy/load = 0 cy (Phase IV & V Scrape) & (Phase IIIB trench excavation). (0 trucks).

- Phase 2 Operations Layer placed. Cumulative total: 37,188 cy.

- Phase 2 estimated cumulative waste placed: 102,106 cy.

Geosynthetics. Estimated cumulative installed quantity by Phase.

- Phase 1 GCL placed: 0 sf daily, 307,372 sf cumulative.

- Phase 1 Geomembrane: 0 sf daily, 307,372 sf cumulative

- Phase 1 Geocomposite: 0 sf daily, 3,372 sf cumulative.

- Phase 1 Geotextile: (0) sf daily, 69,340 sf cumulative.

- Phase 2 GCL placed: (0) sf daily, 498,468 sf cumulative.

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	18-Jan-09	189

-Phase 2 GCL placed: (0) sf daily, 436,468 sf cumulative.
 -Phase 2 Geomembrane: (0) sf daily, 498,468 sf cumulative.
 -Phase 2 Geocomposite: (0) sf daily, 520,592 sf cumulative.
 -BMI North Landfill GCL placed: (0) sf daily, 984,226 sf cumulative.
 -BMI North Landfill Geomembrane: (0) sf daily, 984,266 sf cumulative.
 -BMI North Landfill Geocomposite: (0) sf daily, (425,000) sf cumulative.

Other:

HEALTH & SAFETY

Description of Health & Safety Actions Taken Today / Safety Inspections Conducted

Entact H&S Tailgates

Safety Topic: Eastside, Day: No Activity.

Safety Topic: CAMU, Day: No Activity.

Eastside and CAMU, Night: Safety Proactive and Reactive.

Safety Incidents: None.

Dust Incidents: None.

CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

Description of Quality Control Actions Taken Today / Quality Inspections Conducted	

Daily CQA Summary.

Monitored waste relocation and waste placement from Eastside to CAMU Phase II.

Monitored proofrolling of waste at Phase II.

ISSUES AND/OR ITEMS OF DISCUSSION	
1	1. The first item of discussion is the importance of the study.
2	2. The second item of discussion is the methodology used in the study.
3	3. The third item of discussion is the results of the study.
4	4. The fourth item of discussion is the conclusion of the study.
5	5. The fifth item of discussion is the limitations of the study.
6	6. The sixth item of discussion is the future research.
7	7. The seventh item of discussion is the significance of the study.
8	8. The eighth item of discussion is the contribution of the study.
9	9. The ninth item of discussion is the practical application of the study.
10	10. The tenth item of discussion is the overall impact of the study.

Discussion of Issues / Concerns / Conversations / Topics

SITE VISITORS

[illegible]

Report Prepared By / Title	Date Prepared	Signature
----------------------------	---------------	-----------

Richard Laubinger, Construction Manager 18-Jan-09

Date Prepared	Signature
---------------	-----------

18-Jan-09

Signature _____

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	18-Jan-09	189

DAILY PHOTO LOG

Photo 1

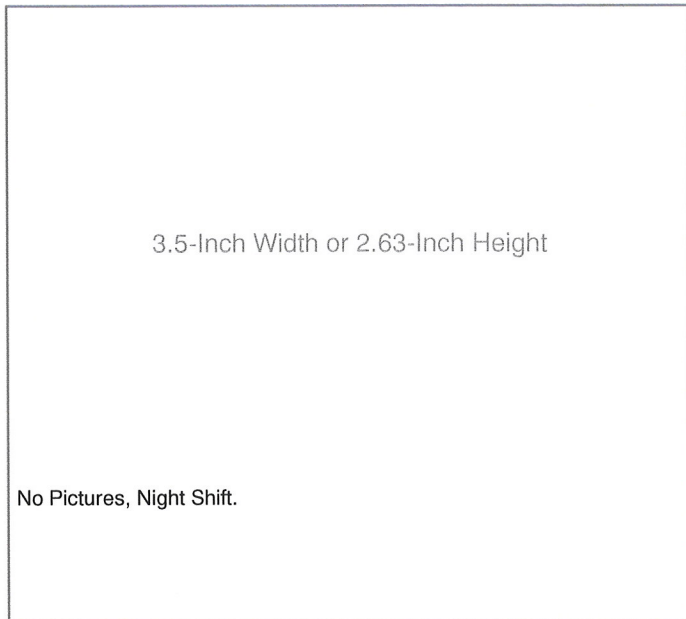


Photo 2



Photo 3



Photo 4

